


# Quarterly Update



## Leading Idaho Local Bridge



### LAST QUARTER SUMMARY

#### Program Updates and Project Advancement

This quarter brought strong progress across the program. Five projects were successfully completed, and nine more were advertised for construction, continuing the steady momentum. In 2026, we also launched a new monthly contractor call to improve coordination and keep partners informed with regular program updates. At the same time, projected obligations are being reviewed to identify opportunities to fund additional projects currently on the wait list, helping us make the most of available resources.

#### Sage Road Over Succor Creek; Homedale Highway District



Bid Opening: March 19, 2026

### FINANCES

#### Turning Funding into Projects

- **\$200 Million** spent of **\$565 Million** obligated toward projects, showing steady progress on program investments.
- **\$75 Million** in payouts completed for State Fiscal Year 2026.
- 58 projects currently under construction, with a total contract value of **\$90 Million**.
- Over **350** contracts executed with engineering and professional services firms.
- **87** construction contracts executed to advance local infrastructure improvements.

#### Funding Progress to Date



COMPLETED PROJECT PICTURES



DIGGER DRIVE OVER  
TETON ISLAND CANAL;  
MADISON COUNTY



POTLATCH ROAD  
OVER  
ELK CREEK;  
SHOSHONE  
COUNTY



WILDHORSE ROAD  
OVER  
WILDHORSE RIVER;  
ADAMS COUNTY




SFY 2026 QUARTER 2 BID RESULTS

FEBRUARY

JANUARY

Key Number	Project Name	Sponsor	\$ Amount
30235	Colburn Culver Road Over Pack River	Bonner County	\$4,747,315.66
29675	Hatter Creek Road Over Palouse River	North Latah County Highway District	\$1,894,860
23373	N 2200 W Over West Cache Canal	Franklin County	\$662,076.76
22035	Hawkins Road over Marsh Creek	Bannock County	\$1,333,176.13
20730	Westside Over Parker Creek	Boundary County	\$1,148,552

BID INSIGHTS

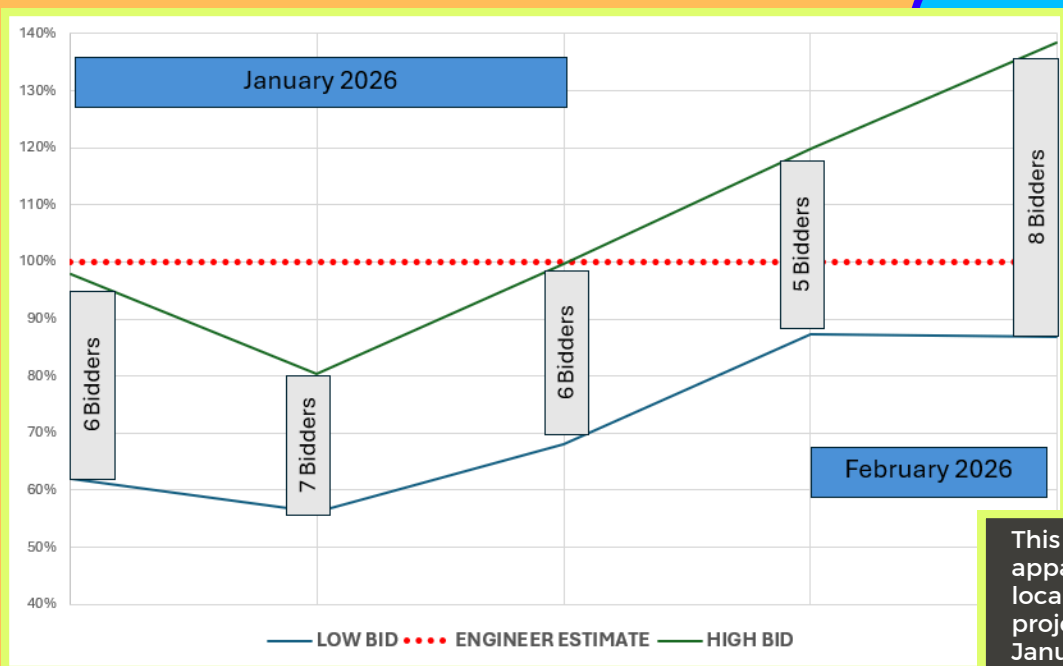

This chart summarizes the apparent bid statistics for local bridge replacement projects received in January and February 2026. No bids in December.

**PROJECT STATUS "BINGO" CHART**

Leading Idaho Local Bridge Program  
Project Status 3/1/2026

2022 Applications															
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	
16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	
46	47	48	49	50	51	52	53	54	55	56	57	58	59	60	
61	62	63	64	65	66	67	68	69	70	71	72	73	74	75	
76	77	78	79	80	81	82	83	84	85	86	87	88	89	90	
91	92	93	94	95	96	97	98	99	100	101	102	103	104	105	
106	107	108	109	110	111	112	113	114	115	116	117	118	119	120	
121	122	123	124	125	126	127	128	129	130	131	132	133	134	135	
136	137	138	139	140	141	142	143	144	145	146	147	148	149	150	
151	152	153	154	155	156	157	158	159	160	161	162	163	164	165	
166	167	168	169	170	171	172	173	174	175	176	177	178	179	180	
181	182	183	184	185	186	187	188	189	190	191	192	193	194	195	
196	197	198	199	200	201	202	203	204	205	206	207	208	209	210	
211	212	213	214	215	216	217	218	219	220	221					


  

2025 Applications															
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	
16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	
46	47	48	49	50	51	52	53	54	55	56	57	58	59	60	
61	62	63	64	65	66	67	68	69	70	71	72	73	74	75	
76	77	78	79	80	81	82	83	84	85	86	87	88	89	90	
91	92	93	94	95	96	97	98								


  

Wait List															
COMPLETE/Posting Removed															
Funded through Federal-aid															
Design/Analysis Phase															
Construction Phase															

**CONSTRUCTION**

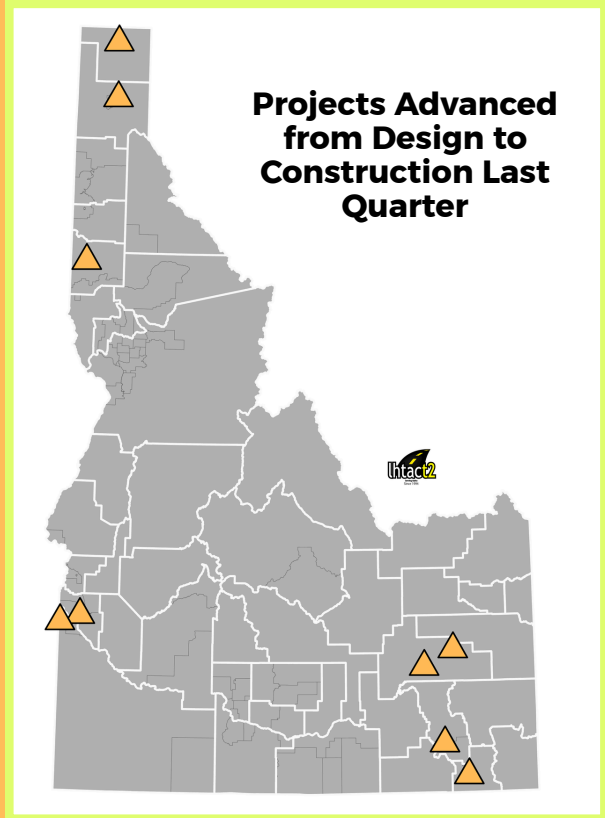

**COMPLETED**

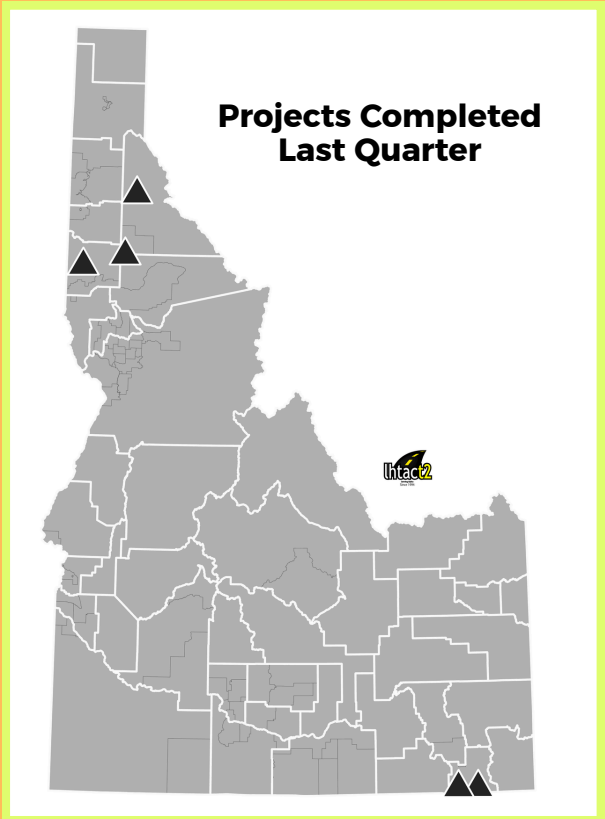

**WAIT LIST**

